

Learning from Demonstration for Complex Tasks: Vision-Language-Action Models for OARbot Control

Pol del Castillo

2026-08-25

Table of contents

1	LfD for Complex Tasks — VLA Control of OARbot	5
1.1	Project schedule	5
1.2	Initiative board	6
1.2.1	A — Foundations — LfD, VLM/VLA, and the task suite	6
1.2.2	B — Platform & data — OARbot bring- up and demonstrations	7
1.2.3	C — Policy learning — GR00T and HF VLA fine-tuning + evaluation	7
1.3	Item board	8
1.3.1	Stale items	8
1.4	Where to go from here	8
I	Background	9
2	Background	10
3	Example section	11
II	Methods	12
4	Methods	13
III	Operations	14
5	Operations	15
6	Fall 2026 Roadmap — experiments to December	16
6.1	Research questions	16
6.2	Compute and platform allocation	17

6.3	Month-by-month plan	17
6.3.1	September — bring-up, task suite, literature (epics B1, A2, A1)	17
6.3.2	October — dataset at scale + first baseline (epics B2, C2)	18
6.3.3	November — GR00T + full evaluation (epics C1, C3)	19
6.3.4	December — finish, freeze, outline (epics C3, D)	19
6.3.5	January–March 2027	20
6.4	Quantifiables — what gets measured and reported	20
6.4.1	Decision thresholds — what “achieved” means	20
6.4.2	Primary metrics (every policy, every task)	21
6.4.3	Secondary metrics	21
6.4.4	Generalization tiers (RQ2)	22
6.4.5	Failure taxonomy	22
6.4.6	Practicality cost sheet (RQ3)	22
6.4.7	Deliverables checklist (results chapter) . .	23
6.5	Literature map	23
6.6	Open-source stack	25
6.7	Using AI research assistants	26
6.8	Risk register	26
6.9	Cadence	28
7	SOP-01: Example procedure	29
7.1	Purpose	29
7.2	Prerequisites	29
7.3	Verification	29
7.4	Change history	29
8	Future work	30
	Appendices	31
A	Weekly updates	31
B	Initiatives	32
C	Archive	33
C.1	Buckets	33

D	External archive index	34
D.1	Always-external (vendor + heavy media)	34
D.2	Oversize files skipped from buckets (> 25 MB)	34

1 LfD for Complex Tasks — VLA Control of OARbot


This site has two halves. The **thesis** is the prose in [Background](#), [Methods](#), [Operations](#), and [Future Work](#) — that’s what gets bound. The rest of the site is the **project-management surface** the thesis runs on: a top-level Gantt, the initiative board below, a weekly-update log, and an archive of source material.

TODO: replace this paragraph with the abstract
once the thesis is drafted.

1.1 Project schedule

Top-level Gantt covering the work categories the advisor tracks. The Mermaid block below is the single source of truth for the schedule. Edit this block when the schedule changes; the per-WU frozen PNGs (`updates/WU-*/media/gantt.png`) regenerate automatically from it via `scripts/render/build_gantt.py`. Add a bar here whenever you scaffold a new epic (`.\thesis.ps1 new epic ...`).

Thesis schedule — experiments to Dec 2026, writing Jan-Feb, defense Mar 2027

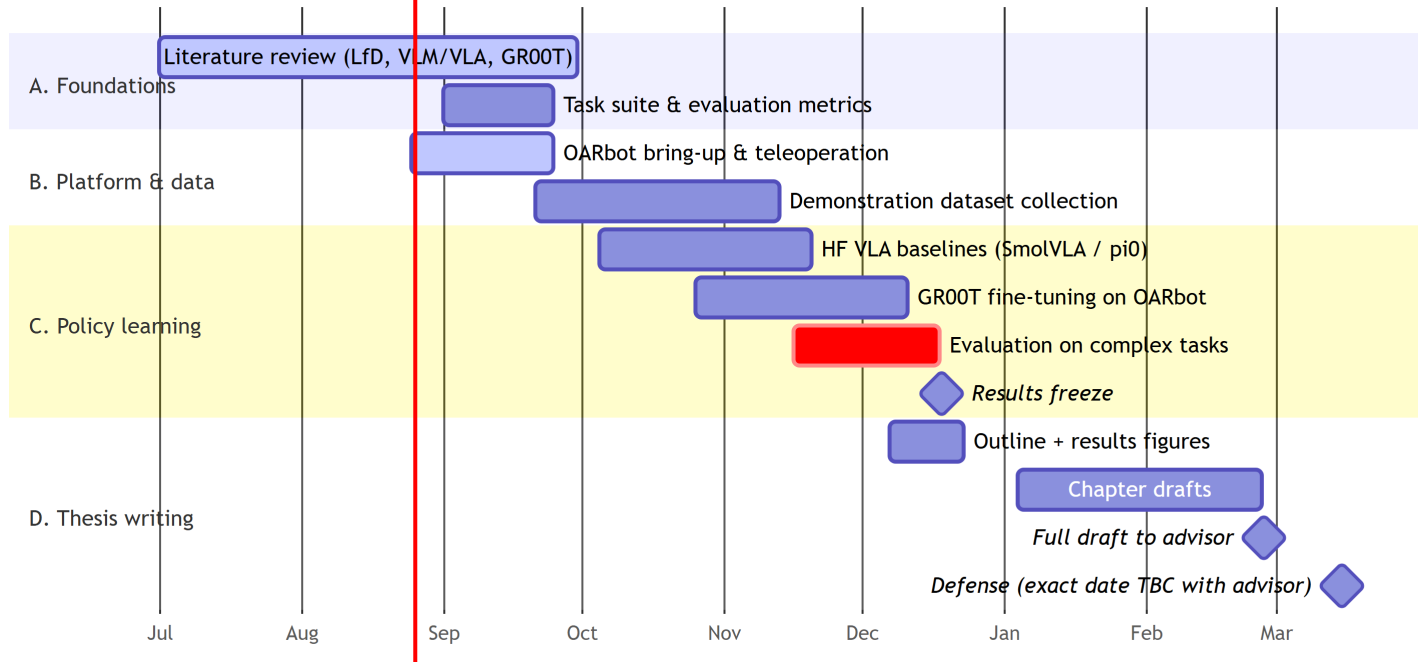

1.2 Initiative board

The Gantt's bars are *epics*. Each epic has a README under [initiatives/](#) with a customer/need/benefit brief, related-epics graph, and an items listing. Everything below is generated from README front matter by `scripts/render/build_board.py` (a pre-render hook) — edit the front matter, never these tables. Schedule emphasis (crit bars) lives in the Mermaid Gantt above.

1.2.1 A — Foundations — LfD, VLM/VLA, and the task suite

Gantt	Epic	Status	Owner
A1	Literature review: LfD, VLM/VLA, GR00T	in-progress	Pol del Castillo
A2	Task suite & evaluation metrics	open	Pol del Castillo

1.2.2 B — Platform & data — OARbot bring-up and demonstrations

Gantt	Epic	Status	Owner
B1	OARbot bring-up & teleoperation	open	Pol del Castillo
B2	Demonstration dataset collection	open	Pol del Castillo

1.2.3 C — Policy learning — GR00T and HF VLA fine-tuning + evaluation

Gantt	Epic	Status	Owner
C1	GR00T fine-tuning on OARbot	open	Pol del Castillo
C2	HF VLA baselines (SmolVLA / pi0)	open	Pol del Castillo
C3	Evaluation on complex tasks	open	Pol del Castillo

1.3 Item board

Open 1

A1-EX-001

Which VLA backbones fit OARbot and the available compute?

A1 · Pol del Castillo

In progress 0

Blocked 0

Done 0

1.3.1 Stale items

in-progress items with no commit in 3+ weeks.

None — every in-progress item has recent activity.

1.4 Where to go from here

- **Reading the thesis** — start with [Background](#) and use the sidebar.
- **Reviewing weekly progress** — see the [weekly updates](#) appendix (newest first).
- **Browsing the project tree** — see the [initiatives](#) appendix; each initiative lists its epics, each epic lists its items + status log.
- **Looking up source material** — see the [archive](#) appendix, with an [external index](#) for files too large to carry in git.

Part I

Background

2 Background

TODO: Part intro — why this research area matters and what question the thesis answers.

3 Example section

TODO: First content section. Chapter subsection files follow the `CH-<N><x>-<slug>.qmd` naming convention and are registered in `_quarto.yml` under `book.chapters`. Cite sources with `@key` against `references.bib`.

Part II

Methods

4 Methods

TODO: Part intro — equipment, experimental setup, and how evidence flows from the lab into the **initiatives/** tree (every experiment in the PM layer that produces thesis-grade results gets written up here).

Part III

Operations

5 Operations

TODO: Part intro for operating procedures. SOPs live in `sops/` and render in three audience variants via Quarto profiles (`--profile sop-detailed | sop-checklist | sop-walkthrough`). Each SOP carries a formal revision block (rendered by the shortcode) plus an auto-generated git change history.

6 Fall 2026 Roadmap — experiments to December

Working plan from today (Aug 25) to the results freeze in December. The [top-level Gantt](#) is the source of truth for dates; this page holds the reasoning behind them: research questions, week-level milestones, the quantifiables spec (metrics, generalization tiers, failure taxonomy), the literature map, the open-source stack, and how AI research assistants are used. Revise it whenever the plan changes — it becomes the skeleton of the Methods chapter and the defense timeline slide.

6.1 Research questions

The thesis claim is built around three questions. Every experiment should answer one of them; anything that doesn't is scope creep.

RQ1 — Adaptation. Can current open vision-language-action (VLA) foundation models (NVIDIA GR00T N1.5, SmolVLA, optionally 0) be adapted to a *new embodiment* — the OARbot (Clearpath Dingo omni base + Kinova Jaco Gen2 6-DOF arm) — with a modest demonstration dataset collected in the lab?

RQ2 — Comparison & generalization. On a fixed task suite, how do the fine-tuned VLAs compare against each other *and against a from-scratch imitation baseline (ACT) trained only on our demonstrations* — both on in-distribution success rate and on how gracefully performance degrades across generalization tiers (unseen poses, distractors, novel object instances, paraphrased instructions)? The baseline is what makes generalization attributable: if the VLAs degrade less than ACT out of distribution, that gap *is* the measured value of internet-scale pretraining.

RQ3 — Practicality. What are the real compute and data costs — fine-tuning wall-clock on a DGX Spark, demos-per-task needed, on-robot inference rates — and what does that imply for small-lab replication?

RQ3 is the differentiator: most VLA papers report results on the authors’ hardware fleet; a careful account of what it takes to adapt these models on one robot with two lab machines is a genuine contribution.

6.2 Compute and platform allocation

Machine	Role
DGX Spark (GB10, 128 GB unified memory)	All fine-tuning: GR00T N1.5 (NVIDIA ships a DGX Spark fine-tuning playbook for it), SmolVLA full fine-tune, 0 LoRA if attempted
RTX workstation (“7080” — confirm exact model, likely RTX 5080)	Robot-side: teleop, data recording, policy inference at eval time, dataset visualization
OARbot helper laptop + Dingo onboard PC	ROS 2 Jazzy stack, drivers, cameras (per the OARbot docs)

Keep training and robot operation on separate machines from day one so data collection never competes with training runs.

6.3 Month-by-month plan

6.3.1 September — bring-up, task suite, literature (epics B1, A2, A1)

- **Week of Sep 1:** Full teleop chain on one OARbot: drive the base, command the arm (SpaceMouse), stream both Azure Kinects. Verify E-stop and deadman behavior. Note

which sensors are actually usable (docs already flag the UWB units as inoperable).

- **Week of Sep 8:** Record demonstrations into **LeRobot-Dataset format** — joint states + base velocity + camera frames, replay a recorded episode open-loop on the robot to prove the pipeline is lossless. This replay test is the single most important de-risking step of the semester.
- **Week of Sep 15:** Freeze the **task suite** (epic A2): 3 tasks in increasing difficulty, e.g. (T1) tabletop pick-and-place, arm only; (T2) fetch — navigate to a table, grasp, return; (T3) a true mobile-manipulation task with base+arm coordination (open a door, clear a table). Define per-task success criteria, the staged **progress rubric** (reach / grasp / transport / place), the in-distribution randomization grid, and the **generalization tiers G1–G4** (see the quantifiables spec below) *before* collecting data. Confirm the suite with the advisor. Also start the **action-space decision log**: every embodiment-design choice (joint deltas vs. absolutes, base twist representation, chunk length, control rates, normalization) gets a dated entry with the reasoning — this log becomes the Methods section on adapting VLA action heads to a mobile manipulator.
- **Week of Sep 22:** Pilot data collection: ~10 episodes per task, train a quick SmolVLA sanity run on T1, fix whatever breaks.
- **Gate 1 (Sep 26):** teleop + record + replay all work, task suite signed off. *Fallback if late: drop T3 base motion and run an arm-centric thesis — decide here, not in November.*

6.3.2 October — dataset at scale + first baseline (epics B2, C2)

- **Weeks of Oct 5 / Oct 12:** Main collection push, target **50–100 episodes per task** (ACT/SmolVLA-class results are routinely reported around 50 demos/task; more helps T3). Interleave tasks and vary object poses per the randomization grid. Nightly QC script: episode counts, joint-limit outliers, dropped frames.
- **Week of Oct 19:** SmolVLA fine-tuned per-task on the Spark, and **ACT trained from scratch on the iden-**

tical data — it trains in hours and rides along on the same LeRobot dataset, giving the no-pretraining reference point for RQ2. First closed-loop rollouts on the robot.

- **Week of Oct 26:** Start GR00T N1.5 fine-tuning (epic C1) — the new-embodiment head needs the most debugging lead time. First structured mini-eval (10 trials/task) of SmolVLA.
- **Gate 2 (Oct 31):** SmolVLA achieves non-zero success on T1 with a documented eval protocol. *If zero: freeze collection, debug the data/normalization/camera pipeline first — more bad data won't help.*

6.3.3 November — GR00T + full evaluation (epics C1, C3)

- **Weeks of Nov 2 / Nov 9:** GR00T N1.5 tuned across tasks; top-up data collection where QC shows gaps; 0 (LoRA via LeRobot/openpi) only if both main models are stable.
- **Week of Nov 16:** Full evaluation begins (epic C3): **20 trials/task/policy** on the shared in-distribution grid, everything in the quantifiables spec logged per trial, video of every trial. Budget realistically — 3 tasks $\times$ 4 policies (ACT, SmolVLA, GR00T, 0-if-attempted) $\times$ 20 trials at ~ 3 min/trial is ~ 12 robot-hours *per full round*, plus resets.
- **Gate 3 (Nov 27):** Decide final comparison set (ACT + 2 or 3 VLAs) and confirm the **data-scale ablation** (retrain at 25/50/100 demos on one task) fits the calendar.

6.3.4 December — finish, freeze, outline (epics C3, D)

- **Weeks of Dec 1 / Dec 7:** Complete in-distribution eval rounds + data-scale ablation; **generalization round** — tiers G1–G4 on each model's best checkpoint only (10 trials/tier, see quantifiables spec).
- **Week of Dec 14:** Re-runs and holes only. **Results freeze Dec 18** — after this date, no new experiments, only analysis.

- **Week of Dec 21:** All results tables and figures generated by script from logged data; chapter outline drafted in chapters/.

6.3.5 January–March 2027

Chapter drafts Jan 4 – Feb 26 (Background and Methods first — most of Methods should fall out of this page and the epic READMEs), full draft to advisor end of February, defense mid-March (confirm the exact date and committee logistics with the advisor **in September**, not January).

6.4 Quantifiables — what gets measured and reported

What the results chapter must contain, modeled on what this class of papers (ACT, Diffusion Policy, OpenVLA, 0, SmolVLA, GR00T, Mobile ALOHA) actually reports. Frozen in epic A2 before data collection; every eval trial logs a row with all of these fields plus a video path.

6.4.1 Decision thresholds — what “achieved” means

Targets are pre-registered thresholds, not promises. A miss, analyzed honestly, is still a result.

- **Platform validated:** 1 policy reaches **70% success on T1** in-distribution.
- **Pretraining transfer confirmed:** the VLAs beat from-scratch ACT on the generalization tiers by **15 percent-age points** average. A null or negative gap = “pretraining did not pay off at this data scale on this embodiment” — a publishable negative result.
- **Practicality documented:** complete cost sheet (below) for every model, no gaps.

6.4.2 Primary metrics (every policy, every task)

Metric	Definition	Reported as
Success rate	Binary per trial against the frozen rubric; human intervention = failure	% with 95% Wilson CI, n = 20
Progress score	Staged credit: reach 0.25 / grasp 0.5 / transport 0.75 / place 1.0 (per-task rubric)	Mean 0–1; separates “never grasps” from “drops at the end” when success rates are low
Time to completion	Successful trials only, start signal → success condition	Median [IQR] seconds

6.4.3 Secondary metrics

Metric	Definition	Reported as
Inference latency	Camera frame in → action chunk out, on the RTX workstation	ms per chunk + achieved control rate (Hz)
Generalization gap	In-distribution success minus per-tier success	Percentage points, per tier per policy
Data efficiency	Success rate at 25 / 50 / 100 training demos (one task, all policies)	Curve — the small-lab money figure

6.4.4 Generalization tiers (RQ2)

Evaluated on each model’s **best checkpoint only**, 10 trials/tier, selection rules frozen in A2:

- **G0** — in-distribution: objects and poses from the training grid.
- **G1** — **spatial**: object poses outside the training grid.
- **G2** — **visual**: distractor objects + lighting change.
- **G3** — **object**: novel instance of the same category (different mug, different box).
- **G4** — **language**: paraphrased instruction, same task (“pick up the cup” → “grab the mug”). VLA-only tier — ACT has no language input, which is itself part of the comparison story.

6.4.5 Failure taxonomy

Every failed trial gets a **first-failure label** from this closed list, logged at eval time (10 seconds of effort) with the video path:

perception/grounding (approached wrong object) · navigation/base-pose (stopped out of reach) · grasp (contact but slip/miss) · manipulation-trajectory (jerky/unsafe motion, joint limit) · instruction (did the wrong task) · stall/timeout · hardware (excluded and retried, not counted).

Rendered as stacked bars per policy × task — this figure explains *why* the success rates differ and is the backbone of the analysis chapter.

6.4.6 Practicality cost sheet (RQ3)

Per model: fine-tuning wall-clock hours and peak memory on the DGX Spark, trainable parameter count (LoRA vs. full), GPU-hours per training run, on-robot inference hardware requirements. Plus data cost: minutes per collected episode, total collection hours, retake rate.

6.4.7 Deliverables checklist (results chapter)

- **T1** Main results: success $\pm$ CI, task $\times$ policy, in-distribution
- **T2** Generalization matrix: policy $\times$ tier
- **T3** Efficiency: latency, control rate, completion time
- **T4** Cost sheet (RQ3)
- **F1** Data-scale curve · **F2** Failure-mode stacked bars · **F3** Qualitative rollout film-strips (best + worst per policy)

Protocol hygiene: the randomization grid and rubrics are frozen before collection; checkpoint selection criteria defined before eval; all runs reported (no cherry-picked seeds); every trial has video.

6.5 Literature map

Organized by the Background chapter’s likely sections. Maintain citations in Zotero and export to `references.bib` (keep BibTeX keys stable). Verify every reference on arXiv/Semantic Scholar before it enters the bib file — never cite from an LLM’s memory.

1. Learning from demonstration — foundations

- Argall, Chernova, Veloso, Browning (2009), *A survey of robot learning from demonstration* — the canonical survey to anchor the chapter.
- Pomerleau (1988), ALVINN — behavioral cloning origin.
- Ross, Gordon, Bagnell (2011), DAgger — compounding-error argument every IL thesis needs.

2. Modern imitation learning architectures

- Zhao et al. (RSS 2023), ACT / ALOHA — action chunking; the direct ancestor of today’s VLA action heads.
- Chi et al. (RSS 2023), Diffusion Policy — generative action heads.
- Lipman et al. (ICLR 2023), Flow Matching — theory behind 0-style and GR00T-style flow action heads.

- Fu, Zhao, Finn (2024), Mobile ALOHA — the closest published setup to this thesis: whole-body IL on a mobile manipulator.

3. Vision-language-action models

- Brohan et al., RT-1 (2022) and RT-2 (2023) — the VLA lineage.
- Open X-Embodiment collaboration (2023/24) — cross-embodiment pretraining; why adapting a generalist to OARbot is plausible at all.
- Octo Model Team (2024) — open generalist policy.
- Kim et al. (2024), OpenVLA — open 7B VLA + fine-tuning recipes (see also the OpenVLA-OFT follow-up on efficient fine-tuning).
- Black et al. (2024), 0; Physical Intelligence (2025), 0.5 — flow matching VLA, open weights via openpi.
- Hugging Face (2025), SmolVLA — small (~450M) VLA designed for exactly this compute class; likely the workhorse baseline.
- NVIDIA (2025), GR00T N1 paper (+ N1.5 release notes) — the primary model; its dual-system architecture and new-embodiment fine-tuning story are directly load-bearing.
- Google DeepMind (2025), Gemini Robotics — closed, but frames the state of the art in Background.

4. Mobile manipulation and assistive context

- TidyBot (2023), HomeRobot/OVMM (2023), BEHAVIOR-1K (2023) — mobile-manipulation task framing and benchmarks.
- RPI’s own OARbot publications — get the list from the advisor; the assistive-robotics motivation should cite the lab’s line of work.

5. Datasets and evaluation methodology

- DROID (2024), BridgeData V2 (2023), AgiBot World (2025) — large-scale teleop dataset practice worth imitating at small scale.
- LIBERO (2023) — task-suite design and eval discipline.

- SimplerEnv — Li et al. (2024), *Evaluating Real-World Robot Manipulation Policies in Simulation* — the real-vs-sim eval gap.
- Recent work on statistically sound robot policy evaluation (trial counts, confidence intervals, A/B protocols) — good target for a deep-research sweep, see below.

6.6 Open-source stack

Resource	Use here
LeRobot	Dataset format, teleop recording, SmolVLA + 0 (PyTorch) training/eval — the backbone of B2/C2
Isaac GR00T	GR00T N1.5 checkpoints + new-embodiment fine-tuning scripts; check NVIDIA’s DGX Spark playbook
openpi	0/ 0.5 reference implementation (JAX) if the LeRobot port falls short
oarbots repo	Lab’s ROS 2 stack, drivers, teleop — extend, don’t rewrite
Hugging Face Hub	Host the OARbot demonstration dataset (private repo) + fine-tuned checkpoints; free provenance and versioning
Weights & Biases (or TensorBoard)	Training curves + eval run tracking, linked from weekly updates
Zotero → <code>references.bib</code>	Single bibliography pipeline into Quarto

Stretch only (explicitly out of scope unless everything lands early): Isaac Lab / SimplerEnv-style sim twin of a task for cheap eval — you have Isaac Sim experience from the SO-101

project, but a sim twin is a second thesis; park it in Future Work.

6.7 Using AI research assistants

Division of labor — each tool where it is strongest:

- **Gemini Deep Research** — breadth: one report per Background section above (“annotated bibliography of VLA fine-tuning on novel embodiments 2023–2026, with arXiv links”). Also the eval-methodology sweep in §5.
- **ChatGPT (deep research)** — cross-check Gemini’s reports; protocol questions (“how many trials for a detectable 15-point success-rate difference between two policies?”).
- **NotebookLM** — load the collected PDFs per chapter section; ask grounded cross-paper questions while writing Background.
- **Claude Code** — everything in-repo: LeRobot/GR00T pipeline code, QC scripts, eval analysis, figures, Quarto chapter drafting, and keeping this PM surface honest.

Standing rule: LLM output is a *lead*, never a *citation*. Every claim that survives into the thesis gets verified against the primary source, and every reference is checked on arXiv before entering `references.bib`.

6.8 Risk register

Risk	Likelihood	Mitigation
Bring-up eats October (drivers, arm, cameras)	High	Gate 1 fallback: arm-only task suite, decided Sep 26

Risk	Likelihood	Mitigation
Demo data too little/noisy for T3	Medium	Tiered tasks — T1/T2 alone still answer RQ1–RQ3; data-scale ablation turns “not enough data” into a finding
GR00T new-embodiment head underperforms	Medium	SmolVLA is the guaranteed baseline; a negative GR00T result, carefully analyzed, is still a thesis result
Eval time underestimated	High	Protocol fixed in Sept; 20 trials budgeted on the calendar, not squeezed in
Generalization round balloons eval time	Medium	Tiers only on best checkpoints, 10 trials/tier; if squeezed, run G1–G4 on T1+T2 only
Two-robot temptation (multi-robot experiments)	Medium	One OARbot is the experiment platform; the second is spare parts / backup until the freeze
Writing starts late	Medium	Section D outline bar in December; Methods accretes from epic READMEs all semester

6.9 Cadence

Weekly update (`.\thesis.ps1 new wu`) every Friday: progress, frozen Gantt snapshot, blockers, questions for advisor. The board and Gantt on the [home page](#) stay the single source of truth — no parallel tracker (Notion/Trello) gets created.

7 SOP-01: Example procedure

7.1 Purpose

TODO: One sentence on what this procedure accomplishes and when it applies. (This SOP exists so the template renders a working example of the revision block + profiles + change history — replace it with your first real procedure.)

7.2 Prerequisites

TODO

7.3 Verification

TODO

7.4 Change history

Owner: TODO Owner

Date	Author	Change
2026-06-12	AmmarBarbee17	Initial commit: Quarto thesis + project-management template

8 Future work

TODO: What the thesis opens up but does not close.
Future-shell epics in the **initiatives/** tree are good
source material here.

A Weekly updates

TODO: Weekly status slides shared with the advisor. Each entry is a standalone revealjs deck. Click any card to open the slides; reveal.js navigation (arrow keys, ESC for overview) applies.

B Initiatives

TODO: Initiatives are the top-level work categories that mirror the sections of the project Gantt. Each initiative groups its epics; each epic groups its experiments, issues, and features.

C Archive

Historical source-of-truth content imported from outside the repo (cloud drives, old proposals, vendor docs). **Large vendor binaries** and pre-hosted media already represented elsewhere are catalogued in [external-index.qmd](#) rather than copied.

C.1 Buckets

Buckets are filesystem dumps under `archive/` — there is no per-bucket rendered page. Use a local clone to browse contents; this table is the inventory. Files over ~25 MB get an external-index entry instead of a copy (git-lfs carries the rest — see `.gitattributes`).

Bucket	Description	Files
<i>(none yet)</i>	TODO: add a row per imported bucket	—

See [external-index.qmd](#) for files that stay at their original cloud paths.

D External archive index

Files referenced by the archive but **not copied into the repo** (too large for git-lfs to carry efficiently, or already represented elsewhere). They remain at their original cloud paths — record the absolute path so future-you can find them.

D.1 Always-external (vendor + heavy media)

What	Location
<i>(none yet)</i>	TODO: e.g. C:\Users\you\OneDrive – University\research\vendor- installers

D.2 Oversize files skipped from buckets (> 25 MB)

File	Size	Source
<i>(none yet)</i>	—	—
